Lab 2 Jira Submission

Agile Backlog Creation and Sprint Simulation in Jira

Student	Ayush Ravindra Paithankar
SRN	PES1UG24CS104
Project	Campus Placement & Internship Pipeline
Sprint	CPIP Sprint 1

This report documents the Agile backlog, story-point estimation, sprint execution, burndown evidence, and reflection for the Jira laboratory exercise. All four required screenshot evidences are included.

Backlog and Sprint Summary

The Campus Placement & Internship Pipeline backlog contains eight user stories across three functional areas. The stories total 37 points and were selected for CPIP Sprint 1.

Story	Functional area	Points	Captured sprint status
Upload and Parse Resume	Student Eligibility & Application	5	Done
Check Placement Eligibility	Student Eligibility & Application	5	In Progress
Register for Placement Drive	Student Eligibility & Application	3	Done
Create Interview Rounds	Interview Management	5	In Progress
Move Candidates Between Rounds	Interview Management	8	To Do
Generate Offer Letter	Offer & Placement Status	5	To Do
View Application Status	Offer & Placement Status	3	Done
Update Placement Status	Offer & Placement Status	3	Done

Sprint State at Capture

The active sprint board shows two stories in To Do, two stories In Progress, and four stories Done. In point terms, 13 points were in To Do, 10 points were In Progress, and 14 points were Done at the time of the screenshot.

Screenshot Evidence 1 Backlog with Epics and User Stories

The backlog view records the eight selected user stories and their association with the Student Eligibility & Application, Interview Management, and Offer & Placement Status functional areas.

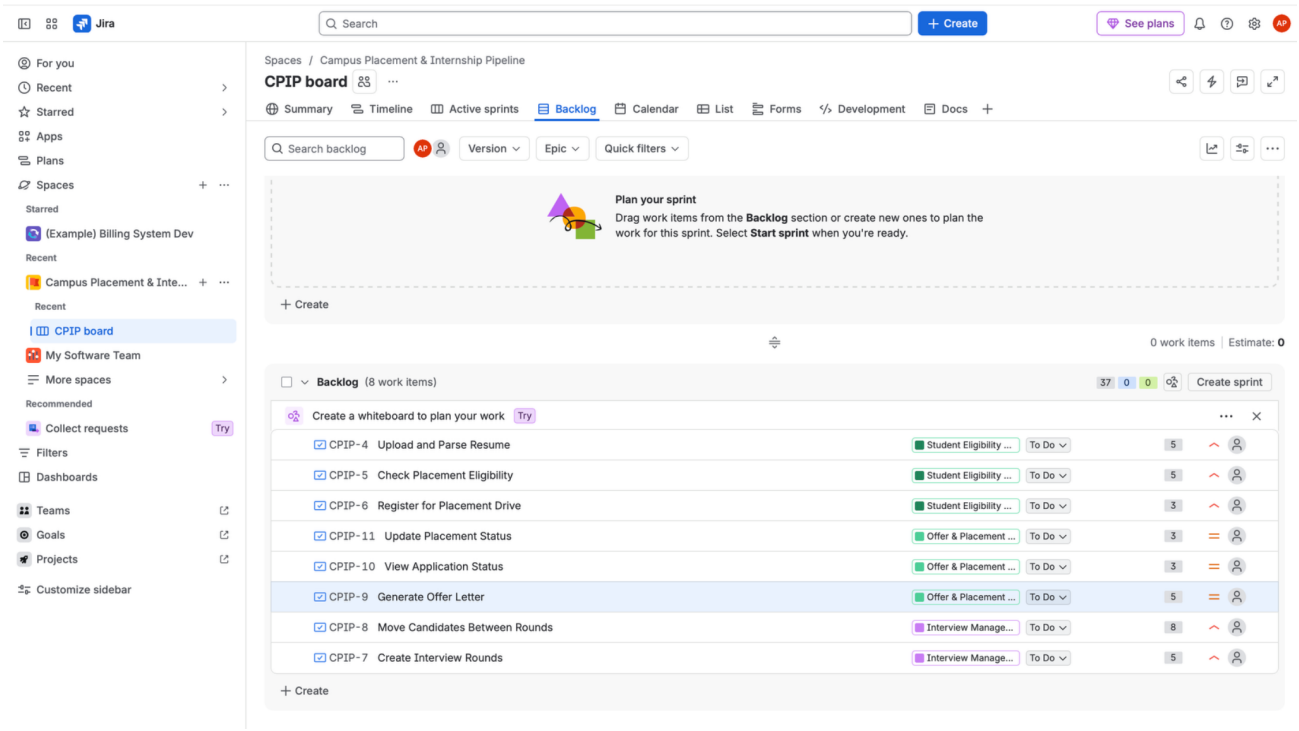


Figure 1 Jira backlog with Epics and User Stories

Evidence Observations

Coverage: All eight work items are visible in the backlog.

Organization: Epic labels group the stories into three clear functional themes.

Prioritization: Priority indicators and backlog ordering are visible for each story.

Screenshot Evidence 2 Story-Point Assignments

The second backlog capture shows the Fibonacci-based point estimate assigned to every user story and the total estimate of 37 points.

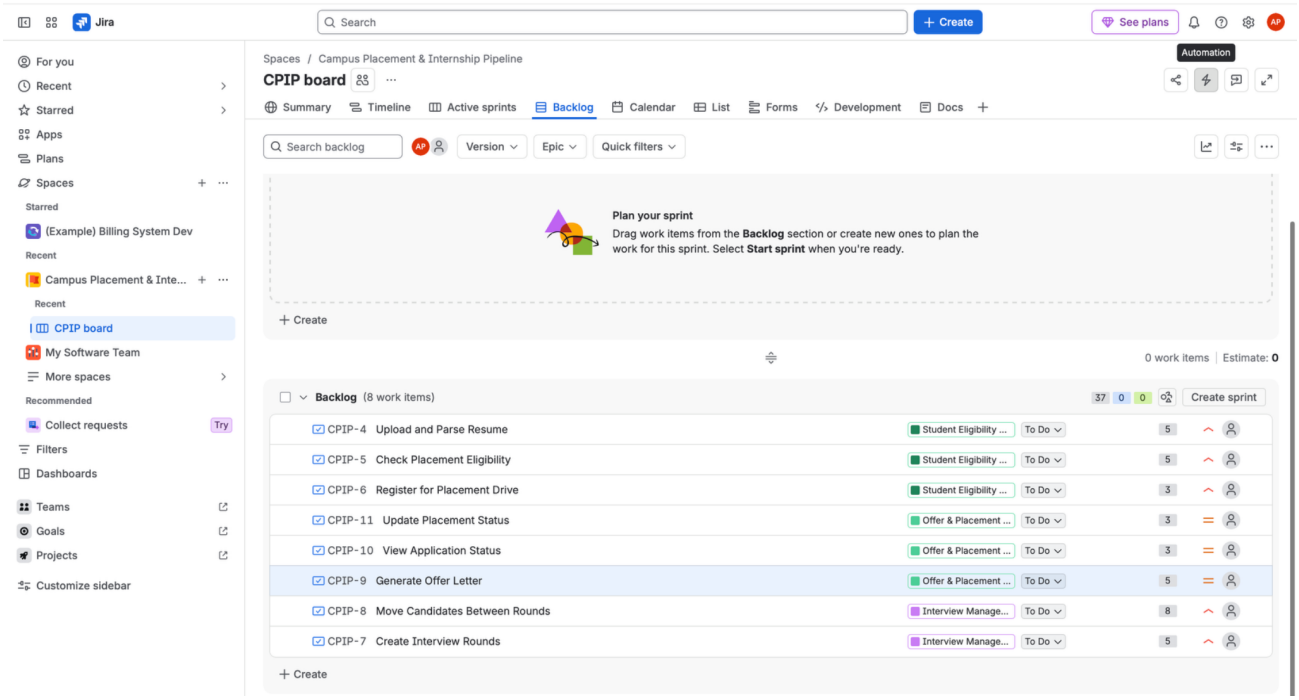


Figure 2 Story-point assignments for the eight backlog items

Evidence Observations

Estimation scale: The visible values are 3, 5, and 8 points.

Largest story: Move Candidates Between Rounds is estimated at 8 points.

Sprint total: The backlog total displayed by Jira is 37 story points.

Screenshot Evidence 3 Active Sprint Board

The active sprint view demonstrates the simulated workflow across To Do, In Progress, and Done for CPIP Sprint 1.

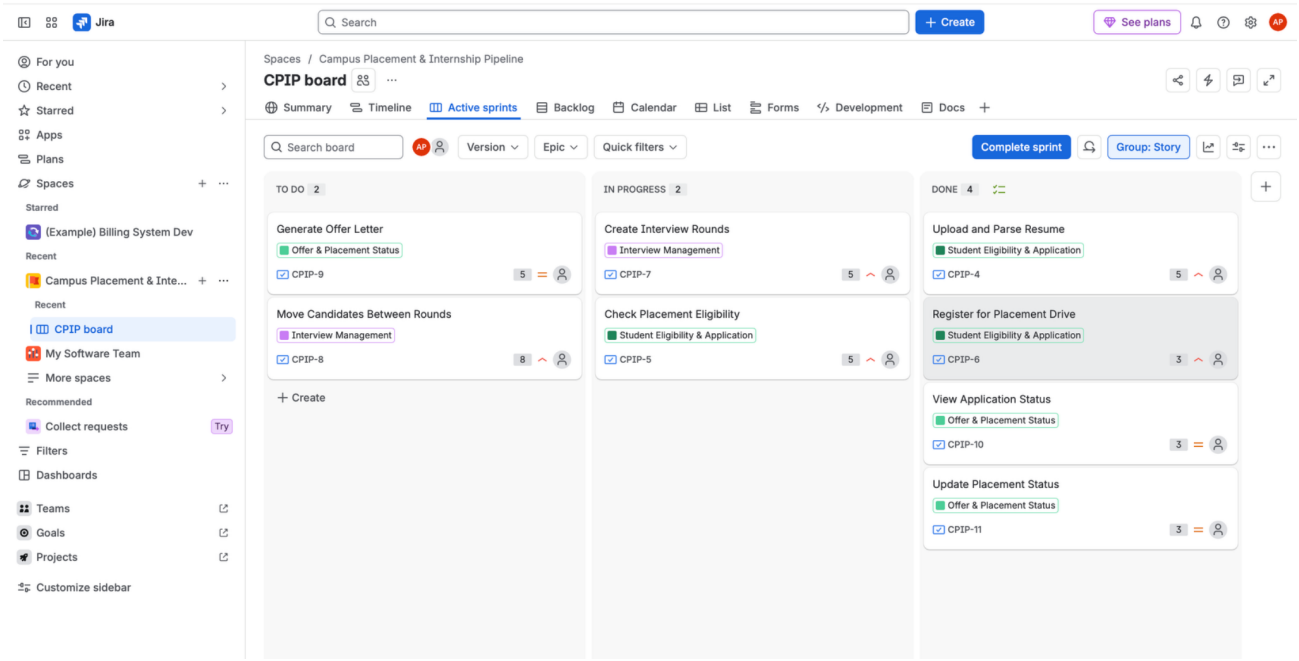


Figure 3 Active Sprint board with work distributed across all workflow states

Evidence Observations

To Do: 2 stories totaling 13 points.

In Progress: 2 stories totaling 10 points.

Done: 4 stories totaling 14 points.

Screenshot Evidence 4 Burndown Chart

The Jira report uses Story Points as the estimation statistic for CPIP Sprint 1 and displays the guideline, remaining values, non-working days, and sprint timeline.

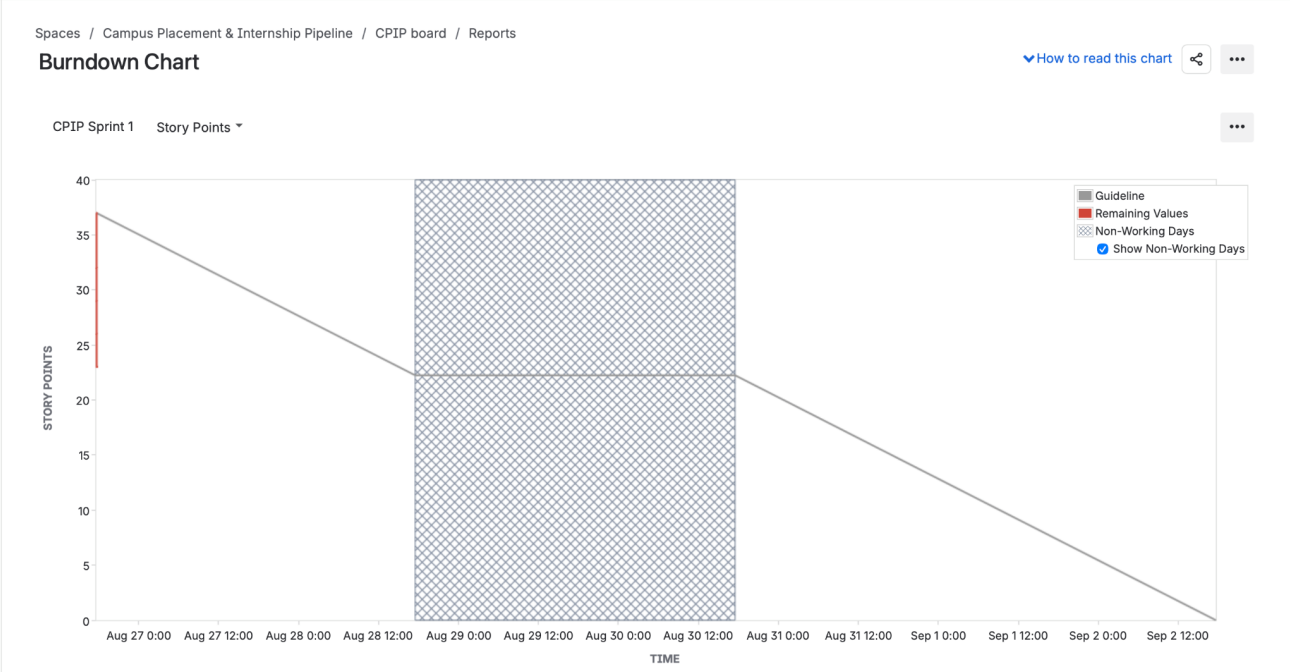


Figure 4 CPIP Sprint 1 Burndown Chart

Evidence Observations

Initial commitment: The chart begins at approximately 37 story points.

Recorded progress: The remaining-value trace shows an early decrease to approximately 23 points.

Timeline: The sprint runs from 27 August through 2 September 2026, with non-working days identified by the hatched region.

Reflection

1 Did your estimations reflect the actual effort?

The estimates provided a useful relative view of effort. Smaller stories were assigned 3 points, most medium-complexity stories were assigned 5 points, and the most complex story was assigned 8 points. The 37-point total created a clear planning baseline, although a real sprint would be needed to compare the estimates with actual development time.

2 Was your backlog well-prioritized?

Yes. The backlog covered the student journey from resume processing and eligibility checks through interview management and offer-status updates. The order reflected functional dependencies and user impact. The backlog could be strengthened further by recording acceptance criteria and an explicit business-value score for each story.

3 How did your simulated sprint align with your plan?

The sprint followed the planned Scrum workflow. At the captured stage, four stories totaling 14 points were Done, two stories totaling 10 points were In Progress, and two stories totaling 13 points remained in To Do. This shows that the work was actively progressing across all three board states rather than remaining entirely in the backlog.

4 What insights did the burndown chart give about your team's capacity?

The chart made the 37-point commitment visible and recorded an early reduction in remaining work. The sharp change suggests that Jira updates were entered in a batch rather than continuously. For a future sprint, daily status updates and smaller stories would create a smoother trend and make the chart a more reliable indicator of capacity and delivery risk.

Conclusion

This lab demonstrated the complete Agile workflow from backlog creation and estimation to sprint execution and progress monitoring. The evidence confirms that eight user stories were organized across three functional areas, estimated at 37 points, moved through the sprint board, and monitored with a Jira Burndown Chart.
